

## THE DESCRIPTION OF PERSONS AND ADDRESS OF THE PERSONS AND ADDRESS AND AD



## Transmission Projects Update

NPPD Board of Directors Meeting Customer & Support Services Committee December 2024

Scott Walz, Vice President Energy Delivery



### R-Project 345 kV Transmission Project

- NPPD continues to respond to information requests from USFWS as they continue to work through permitting process
- Continue to work with the USFWS to complete Section 106 of the National Historic Preservation Act
- The USFWS continues the government-to-government consultation with tribal communities

• Budget: \$399,799,154

Spent to Date: \$149,213,903

(as of 11/30/24 – lines only)

Record of Decision – August 2025

In-service date: December 2027

## **Kearney Tower-Kearney Tech One 115 kV Transmission Line Project**

- Easement acquisition continues:
  - Total easements to acquire = 25
  - Easements acquired = 23
- Watts Electric continues to frame and set poles, clear right-of-way, and receive steel poles
  - Construction 8% complete
- Construction Start: October 2024
- In-service: May 2025
- Budget: \$11,915,911 Spent to Date: \$4,838,849 (as of 11/30/24)




## Scottsbluff-Victory Hill 115 kV Transmission Line Project

- Easement acquisition continues:
  - Total easements to acquire = 61
  - Easements acquired = 60
- Watts Electric continues to frame and set poles, clear right-of-way, and install pier foundations
  - Construction 10% complete
- Material being delivered to construction site

- Construction Start: October 2024
- In-service: May 2025
- Budget: \$16,459,293 Spent to Date: \$7,708,727 (as of 11/30/24)

## Scottsbluff-Victory Hill 115 kV Transmission Line Project

#### Construction Pictures:

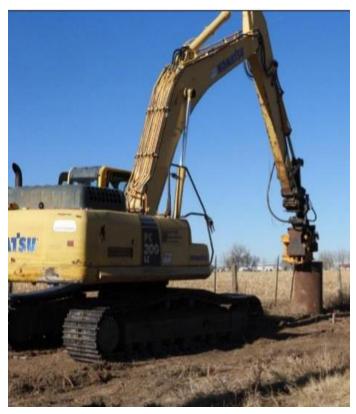





### Norfolk - Stanton North 115 kV Transmission Line Project

- Easement development and acquisition:
  - Total easements to acquire = 27
  - Easement packages released to ROW Agents = 17
  - Easements acquired = 3
- Advertised Request for Bid for tree clearing
- Engineering is at 90% complete

- Construction Start: July 2025
- In-service Date: November 2025
- Budget: \$11,943,091

Spent to Date: \$1,191,029

(as of 11/30/24)



# 



#### Questions

Stay connected with us.







