



THE POWER OF PEOPLE



Transmission Projects Update

NPPD Board of Directors Meeting
Operations Committee
January 2025

Scott Walz, Vice President Energy Delivery



Nebraska Public Power District
Always there when you need us

R-Project 345 kV Transmission Project

- NPPD continues to respond to information requests from USFWS as they continue to work through permitting process
- Continue to work with the USFWS to complete Section 106 of the National Historic Preservation Act
- The USFWS continues the government-to-government consultation with tribal communities

- Budget: \$399,799,154

Spent to Date: \$150,306,573

(as of 01/07/25 – lines only)

- Record of Decision – August 2025

In-service date: December 2027

Kearney Tower-Kearney Tech One 115 kV Transmission Line Project

- Easement acquisition continues with 96% (24 of 25) of easements acquired
- Watts Electric began to pour foundations and continues to frame and set poles, clear right-of-way, and receive conductor
 - All steel poles have been received
 - Construction - 12% complete

- Construction Start: October 2024
- In-service: May 2025
- Budget: \$11,915,911 Spent to Date: \$7,207,537 (as of 1/07/25)

Kearney Tower-Kearney Tech One 115 kV Transmission Line Project

- Construction Photos:




Scottsbluff-Victory Hill 115 kV Transmission Line Project

- Easement acquisition completed (61 of 61 easements)
- Watts Electric continues to frame and set poles, clear right-of-way, install pier foundations, and receive steel poles
 - All conductor has been delivered
 - Construction - 40% complete

- Construction Start: October 2024
- In-service: May 2025
- Budget: \$17,809,229 Spent to Date: \$8,960,128 (as of 1/07/25)

Scottsbluff-Victory Hill 115 kV Transmission Line Project

Construction Photos:

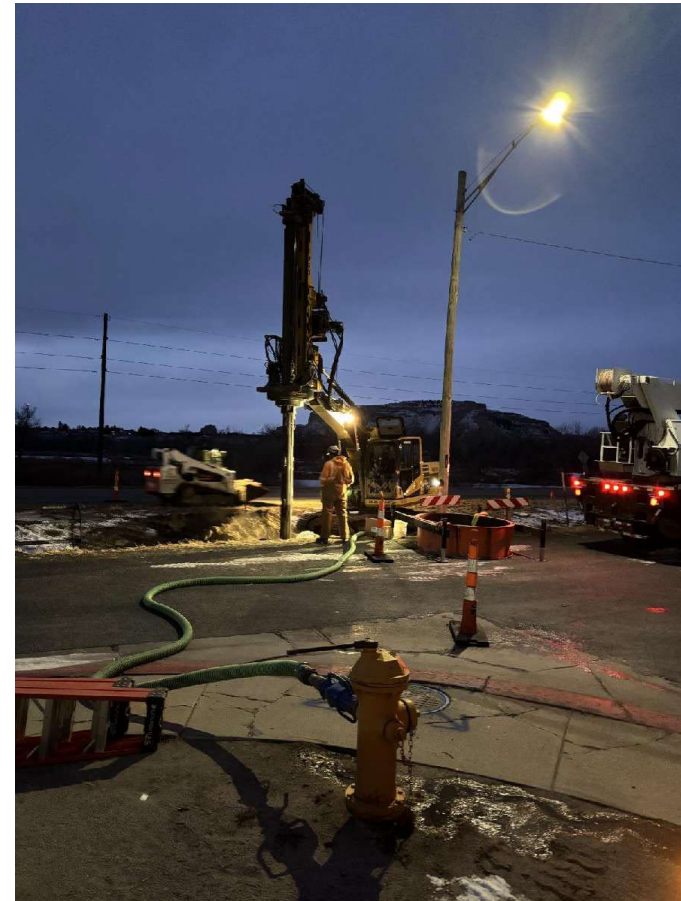

Norfolk – Stanton North 115 kV Transmission Line Project

- Easement acquisition continues with 37% (10 of 27) of easements acquired
- Advertised Request for Bid for tree clearing
 - Tree clearing to begin in February
 - Newsletter is being prepared to advise landowners of the upcoming work
- Engineering is at 90% complete

- Construction Start: June 2025
- In-service Date: November 2025
- Budget: \$11,943,091

Spent to Date: \$1,462,352 (as of 1/07/25)



THE POWER OF PEOPLE



Questions

Stay connected with us.



Nebraska Public Power District

Always there when you need us
