



THE POWER OF PEOPLE



Transmission Projects Update

NPPD Board of Directors Meeting
Operations Committee
April 2025

Scott Walz, Vice President Energy Delivery



Nebraska Public Power District
Always there when you need us

R-Project 345 kV Transmission Project

- NPPD continues to respond to information requests from U.S. Fish and Wildlife Service (USFWS) as they continue to work through permitting process
- NPPD and USFWS participated in bi-weekly project meetings on March 13 and 27
- Continue to work with the USFWS to complete Section 106 of the National Historic Preservation Act
- Eagle surveys conducted on April 3, via helicopter, to support future construction
 - Landowners who have signed easements were contacted and advised of the survey. No issues were raised by landowners.

R-Project 345 kV Transmission Project

- Violet surveys to occur in May to gather habitat information should the Regal Fritillary butterflies be listed as a threatened species (butterflies feed off of the violet). Landowners will be contact accordingly.

- Budget: \$638,000,051

Spent to Date: \$152,086,452

(as of 04/01/25 – lines only)

- Record of Decision – October 2025

In-service date: December 2027

Kearney Tower-Kearney Tech One 115 kV Transmission Line Project

- Construction is 60% complete:
 - Foundation installation complete
 - Continue to set poles and clear trees
 - Began stringing conductor
 - Anticipate construction to be completed May 30
 - Conducting daily whooping crane surveys
-
- Construction Start: October 2024
 - In-service: May 2025
 - Budget: \$11,915,911 Spent to Date: \$8,991,054 (as of 4/01/25)

Kearney Tower-Kearney Tech One 115 kV Transmission Line Project

- Construction Photos:




Scottsbluff-Victory Hill 115 kV Transmission Line Project

- Construction is 80% complete:
 - Structure installation is complete
 - Began stringing conductor
 - Anticipate construction to be completed June 13
- Construction Start: October 2024
- In-service: June 2025
- Budget: \$17,809,229 Spent to Date: \$12,782,233 (as of 4/01/25)

Scottsbluff-Victory Hill 115 kV Transmission Line Project

Construction Photos:

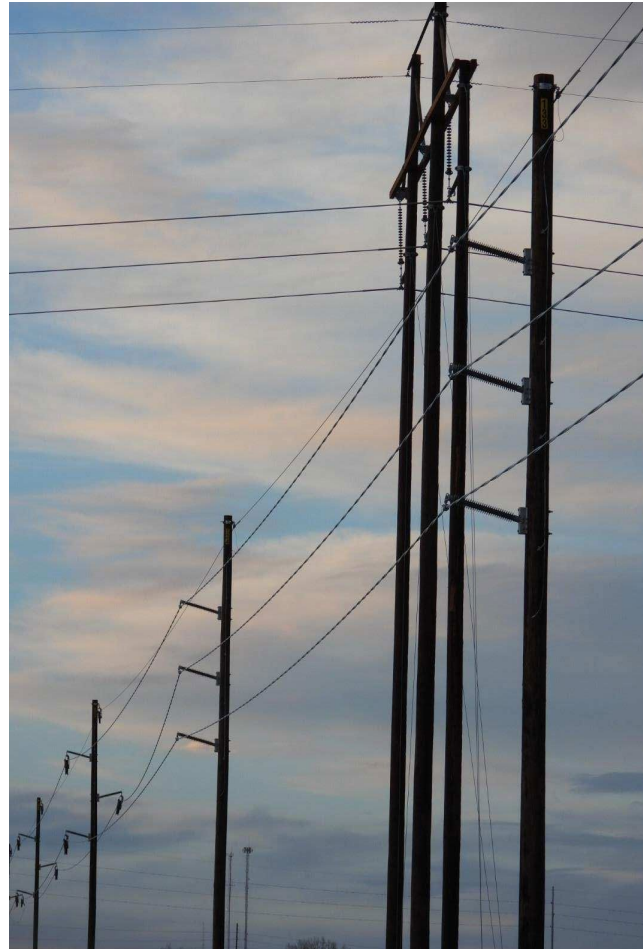

Norfolk – Stanton North 115 kV Transmission Line Project

- Easement acquisition continues with 67% (18 of 27) of easements acquired
 - Tree clearing work began February 24
 - Engineering is 95% complete
 - Foundation contract to be awarded on April 10
 - Anticipate foundation work to begin on June 2 and the remaining construction in July
-
- Construction Start: June 2025
 - In-service Date: November 2025
 - Budget: \$11,943,091
- Spent to Date: \$1,918,971 (as of 4/01/25)



THE POWER OF PEOPLE



Questions

Stay connected with us.



Nebraska Public Power District

Always there when you need us
