

## Transmission Projects Update

THE PEOPLE STATES OF THE PEOPL



NPPD Board of Directors Meeting

Operations Committee

September 2025

Scott Walz, Vice President Energy Delivery



## R-Project 345 kV Transmission Project

- NPPD continues to respond to information requests from U.S. Fish and Wildlife Service (USFWS) as they continue to work through permitting process.
- NPPD and USFWS participated in project meetings on August 6<sup>th</sup> and August 28<sup>th</sup> to discuss programmatic agreement and other project related items.
- Continue to work with the USFWS to complete Section 106 of the National Historic Preservation Act.
- Tribal coordination meeting for the programmatic agreement held on August 28<sup>th</sup>.

Record of Decision - October 2025 Budget: \$721,487,000 In-service date: September 2028 Spent to Date: \$173,301,081 as of (09/02/25- lines & subs)

### Norfolk - Stanton North 115 kV Transmission Line Project

- Construction is 46% complete
- Setting drilled pier foundation steel poles
- Setting direct embed steel poles
- All wood poles are framed and standing
- Tree clearing continues

Construction Start: June 2025


Budget: \$11,943,091

In-service Date: November 2025

Spent to Date: \$6,310,492 (as of 09/02/25)

## Norfolk - Stanton North 115 kV Transmission Line Project

#### Construction Photos:

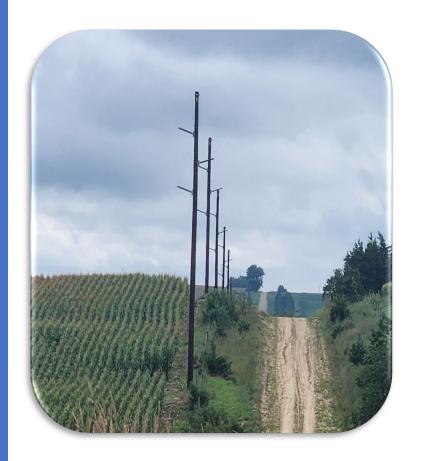







# THE POPULATION OF PROPERTY OF THE POPULATION OF



## Questions

Stay connected with us.







